ID	Description	Start	Finish
Salina Intermediate Recreation Field		07/02/26	04/09/27
Pre-Construction		07/02/26	08/10/26
10	Bidding	07/02/26	07/20/26
20	Post Bid Interview	07/20/26	07/20/26
30	Board Recomendation Letter	07/20/26	07/20/26
40	Board Approval	07/27/26	07/27/26
50	Contracts	07/28/26	08/10/26
Procurement		08/11/26	10/19/26
60	Submittals (GC & Architect)	08/11/26	08/31/26
70	Permits	08/11/26	08/11/26
80	Mobilization, Staking Utilities, Temp Fencing	08/11/26	08/17/26
90	Alternate #1 Pergola Materials	09/01/26	10/05/26
100	Alternate #2 Greenhouse	09/01/26	10/19/26
Construction		08/18/26	03/26/27
110	Protect Existing Trees & Utilities	08/18/26	08/18/26
120	Site Demolition	08/19/26	09/01/26
130	Remove Existing Storm Sewer & Structures	09/02/26	09/03/26
140	Underground Storm, Catch Basin, & Man Hole	09/04/26	09/17/26
150	Underground Inspection	09/18/26	09/22/26
160	Backfil and Compaction	09/23/26	09/24/26
170	Testing	09/25/26	09/25/26
180	Rough Grading	09/28/26	10/09/26
185	Irrigation System (Issued in Addendum)	09/28/26	10/09/26
190	Concrete Walks, Curb & Asphalt Pavement	10/12/26	10/23/26
200	Proof Roll/Testing/Final Grade	10/12/26	10/23/26
210	Alternate #1 Greenhouse Install	10/20/26	11/09/26
220	Alternate #2 Pergola	10/06/26	10/19/26
230	Winter Conditions	10/26/26	03/12/27
250	Remove Temp Fencing	03/15/27	03/15/27

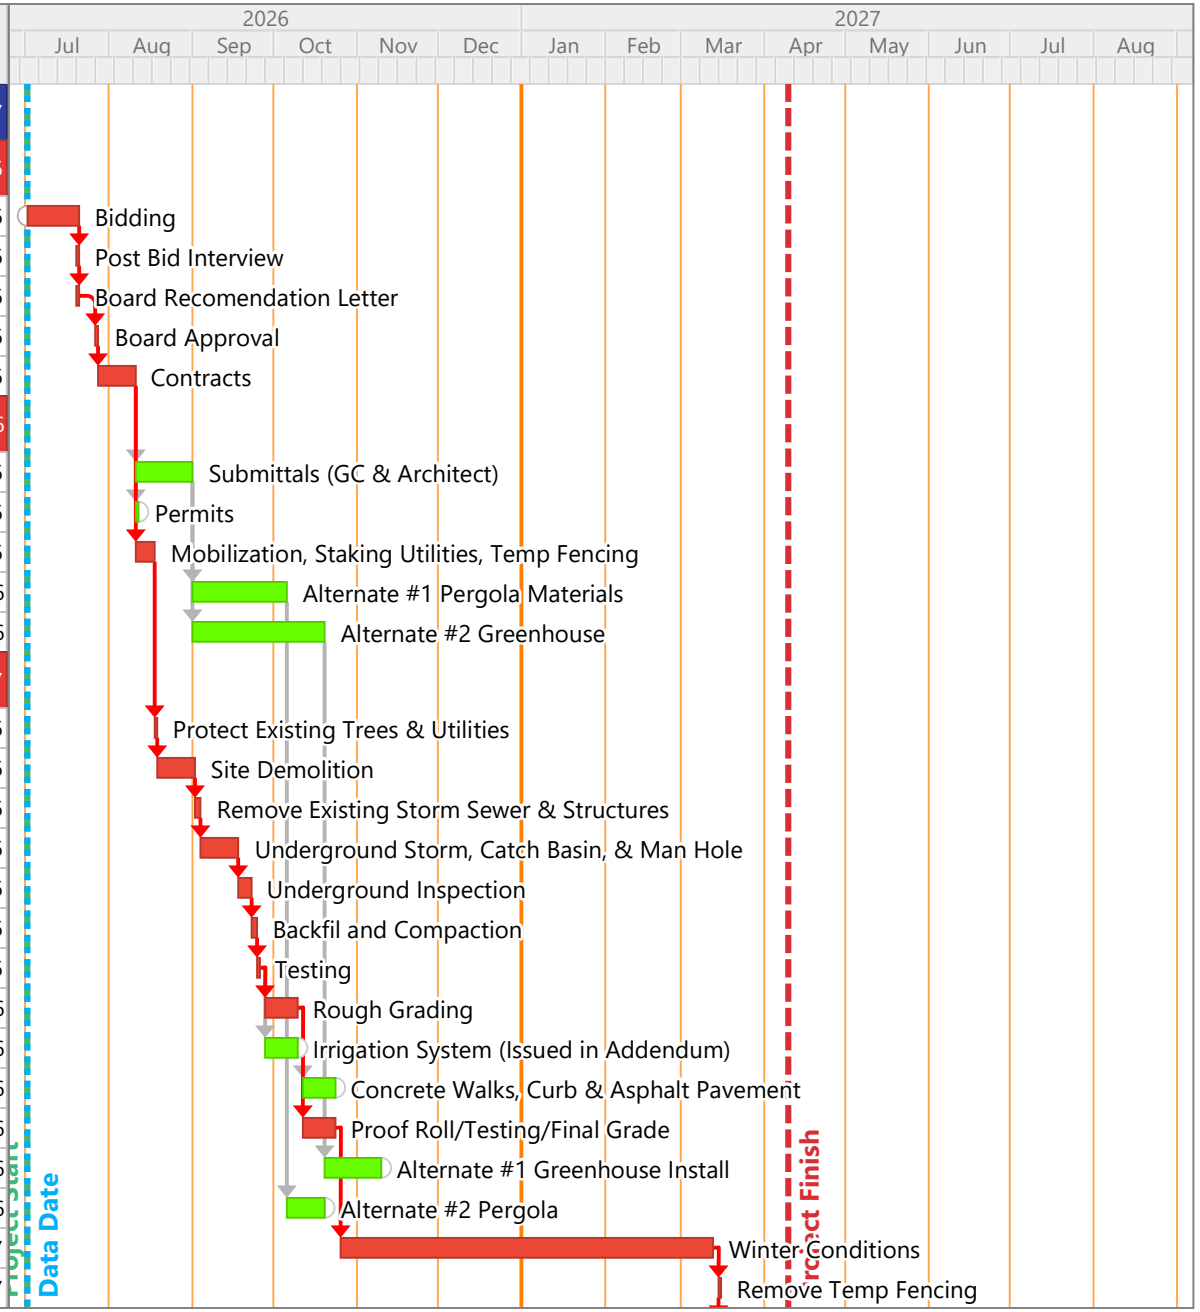

Start Date: 07/02/26
Finish Date: 04/09/27
Data Date: 07/02/26
Run Date: 07/02/26
Salina Intermediate Recreation Field Update.ppx

DEARBORN SCHOOLS

ID	Description	Start	Finish
260	Tree Planting	03/15/27	03/16/27
270	Engineered Wood Fiber	03/17/27	03/17/27
275	Top Soil & Seeding.	03/17/27	03/23/27
280	Boulder Placement	03/17/27	03/17/27
290	Black Chain Link Install	03/22/27	03/26/27
Closeout		03/29/27	04/09/27
300	Closeout Documents	03/29/27	03/29/27
305	Street Cleaning	03/29/27	03/29/27
310	Final inspections as required	03/29/27	03/29/27
320	Punchlist	03/29/27	04/09/27

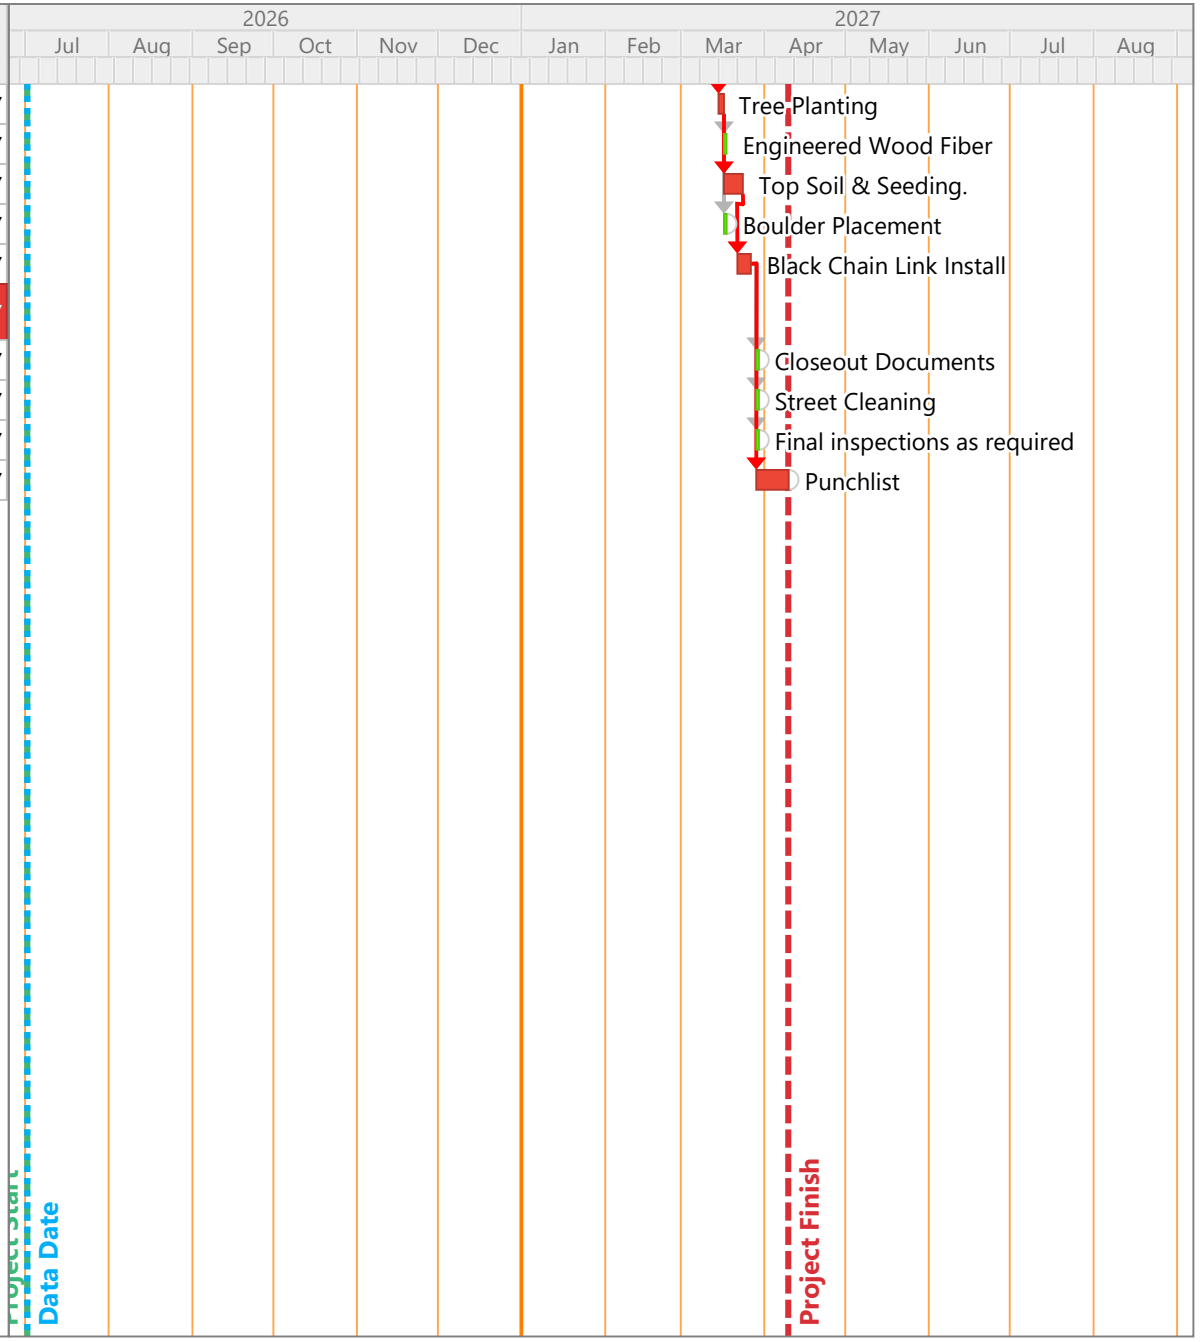

Start Date: 07/02/26
Finish Date: 04/09/27
Data Date: 07/02/26
Run Date: 07/02/26
Salina Intermediate Recreation Field Update.ppx

DEARBORN SCHOOLS
